


SR 44 Repaving from US 19 to NE 10th Ave. 441665-1-52-01

Project Details	
Work Type	Resurfacing
Phase	Completed
Limits	from US 19 to east of NE 10th Ave.
Project Start	November 7, 2022
Length	0.6 miles
City	Crystal River
County	Citrus
Road	SR 44 US 19
Construction Cost	\$3.1 million
Estimated Completion	Summer 2023
Contractor	C.W. Roberts Contracting, Incorporated

Contact Information	
Project Information	John McShaffrey 813-975-6930 roadwork@dot.state.fl.us
	Media Contact Kris Carson 813-975-6060 Kristen.Carson@dot.state.fl.us

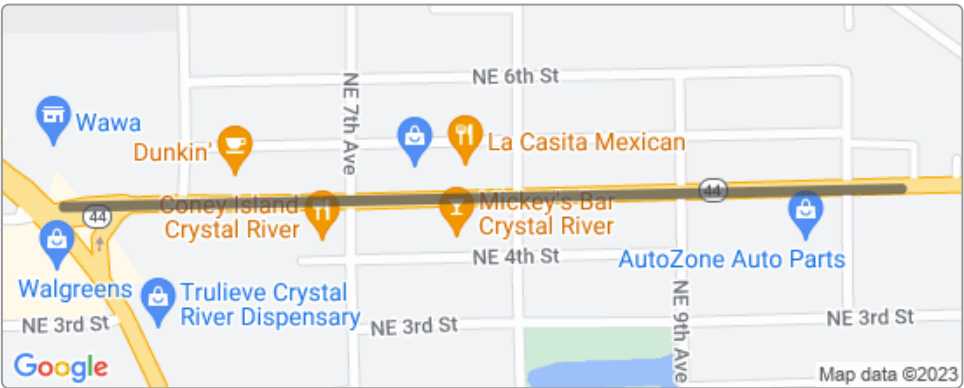

About

As of June 14, 2023, all work was completed and this project was final-accepted from the contractor.

This project repaved SR 44 between US 19 and NE 10th Ave. in Crystal River. Additionally, raised medians with dedicated left-turn lanes and mid-block pedestrian crossings were added. The bike lane widths were increased to 5-feet, an 8-foot sidewalk was added to the north side of the roadway, and the existing sidewalk on the south side was repaired, including filling gaps where there was available right of way.

The signalized intersection was improved at US 19 and SR 44, and a new signal was installed at SR 44 and NE 8th Avenue (Dr. Martin Luther King Jr. Avenue).

TRAFFIC SIGNAL UPDATE: The new signal at SR 44 and NE 8th Avenue (Dr. Martin Luther King Jr. Avenue) was put into operation on March 1, 2023.
